

SS 177 7/96

STATE OF WEST VIRGINIA

INSPECTION TO BE
PRINTED OR TYPED

HEALTH DEPARTMENT

Permit No.: ST-14-068

Tax Map: 23 Parcel #:

County Road:

County: Hampshire

ON-SITE SEWAGE DISPOSAL SYSTEM
INSPECTION FORM

Name of Owner: Jim + Susan Miller Installer: WATER FIELD

Address: P.O. Box 359 Romney WV 26757

Property Location: River Ridge lot #1

Type of Facility: HOUSE Facility is: New (X) Existing () Lot Size: 20 - Sq. Ft.

Design Loading in gpd/No. Bedrooms: 3BR Source of Water Supply: well

SEWAGE TANK COMPONENT

Capacity in Gallons: 1000 Material: concrete Manufacturer: STS

Distances (in feet) of Tank to: Dwelling: Private ()/Public () Water Source: Property Line:

ON-SITE DISPOSAL SYSTEM

Class I Systems: Standard Soil Absorption Trenches () or Bed () Gravelless Pipe (), Diameter: In
Chamber Soil Absorption Trenches (X) or Bed ()Class II Systems: Pumped/Dosed Soil Absorption Trenches () or Bed () Evapotranspiration Trenches () or
Shallow Soil Absorption Trenches () or Bed () Other:

No. of Lines: 3 Length (in feet) of Each: 80, 80, 80

Width of Trenches: 36 inches/feet Depth to Bottom of Field: 24 inches

If Bed, Dimensions (in Feet): If Chamber System, Name: BIO, No. of Units:

Approved and Adequate Materials Used? Yes (X) No () Size Equates to: 1200 Square Feet of Standard Gra

Distances (in feet) of System to: Dwelling: Private ()/Public () Water Source: Property Line:

Remarks:

An inspection indicates that the sewage disposal system described above


DOES MEET (X),
DOES NOT MEET (),
CANNOT BE DETERMINED TO MEET () the minimum standards established by the West Virginia Bureau of Public Health.

To correct a health hazard, modifications to existing systems may be done to improve part of a system. Such modifications may not be able to be designated as a does meet system since inadequate information is known.

Although many factors contribute to the successful functioning of a sewage disposal system, this office recommends water conservation and maintaining an even usage of water throughout the week.

Sketch of Installation with Triangulation or Distance to Specific Landmarks

12-6-05
No well
No house

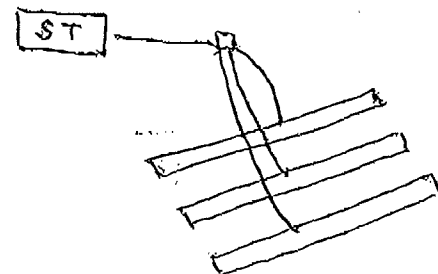

NOT TO SCALE

Visit Date(s): 7-2-05

Final Inspection Date: 12-6-05

Sanitarian: J. Kuntz
