

SW258

Date(s) 4/19/93 County Hampshire Permit #: DW-14-03-93-211
Town: _____ Area Name/Location Whitsons Point Lot 29
Well Owner: Roscoe B. Gunn Address: 637 6th St.
Telephone Number: 822-3306 Romney WV. 26757
Well Driller: B. Mark Smith Address: HC 86 Box 2-A
Telephone Number: 822-4786 Springfield WV. 26763
WELL LOG _____

DEPTH IN FEET	FORMATIONS: KIND, THICKNESS, AND IF WATER BEARING	REMARKS:
0-83	Clay & Boulders	well was cased to bottom w/ 4" pvc well casing bottom 20' perforated - pump set at 240 Type of Well: <u>home</u> Drilling Method: <u>Air hammer</u> Well Diameter: <u>6"</u> Casing O.D.: <u>6 5/8"</u> Well Depth: <u>265</u> Date Completed: <u>4/19/93</u> CASING: Length <u>107</u> Feet Height above ground <u>1</u> Feet <input checked="" type="checkbox"/> Steel <u>GALV.</u> <input type="checkbox"/> Plastic <input type="checkbox"/> Cast Iron Other _____ Type _____
84-138	Driskany Sandrock	
139-142	Soft Spot (Fractured)	
143-209	Driskany Sandrock	
210	Water	
211-265	Driskany	SCREEN <input checked="" type="checkbox"/> None Installed Type _____ Diameter _____ Slot/Gauge _____ Length _____ Set Between _____ Ft. and _____ Ft.
420 Gph		

DETAILS	#1	#2	#3
Static Water Level (Ft. Below Grade)	130		
Pumping Rate (GPM)	7		
Pumping Level (Ft Below Grade)	255		
Duration of Test (In Hours)	1		
Recovery Time to Static Level (In Hours)	1		

Pitless Adapter: Type, Make, Etc. _____
Well Cap: Type, Make, Etc. Standard
Well Seal: Type, Make, Etc. _____
Well Platform: _____
Length _____ Width _____ Thickness _____
Grouting: ☒ Yes ☐ No
All Public Water Supplies must be grouted.

B. MARK Smith
Name B.W. Smith Well Drilling
Registered Business Name Benjamin Mark Smith
Signed Date

SS-177

Revised 1-71

WEST VIRGINIA
SEPTIC TANK INSPECTION FORM

Hampshire County Health Department Installation Permit No. ST-14-12-475
 Name of Owner Roscoe B. Dunn
 Address 637 - 6th St., Romney, WV
 Property Address Whitson Point Lot #27

DESCRIPTION & NUMBER OF UNITS SERVED

Type Facility Served residence No. Water Closets
 Lot Size 2.42 acres sq. ft. Area suitable for sewage disposal installation sq. ft.
 Source of Water Supply future well No. Lavatories
 No. Bedrooms 1 No. Showers or Tubs No. Baths
 No. Garbage Grinders 0 No. Automatic Washers 0

SEPTIC TANK

Material (polin) concrete Length x Width x Depth = cubic feet
 Liquid Depth ft. Liquid Capacity 1000 gal.
 Distance to: Dwelling 9' Water Supply 100' Nearest Property Line 50'

SOIL ABSORPTION SYSTEM

Type Drain Line Material gravelless Trench Width 24 Inches
 Trench Depth 24 Inches Total Absorption area in Trench Bottom 600 sq. ft.
 Diameter of Drain Line 10 Inches Type Filter Media
 No. of Drain Lines 2 Depth Filter Media Under Drain Line Inches
 Length of Each Line 100, 100, , ft. Depth Filter Media Over Drain Line in
 Distance of Disposal Field to: (a) Dwelling 20'
 (b) Water Supply 100' (c) Nearest Property Line 10'

An inspection of the septic tank system described herein disclosed that said system MEETS (MEETS, DOES NOT MEET) the minimum standards established by the West Virginia State Department of Health.

Date

5-19-92

Sanitarian

Lee O'Han


SKETCH OF SYSTEM TO BE DRAWN ON BACK

Note: Copy of this inspection report must be given to owner and the original filed in the Health Department files. PERMANENT RECORD - DO NOT DESTROY.

* Due to space limitations, tank is 9' instead of 10' from house. This is accepted as unavoidable at site.

PROP. LINE

Whitson's Point
Lot 27

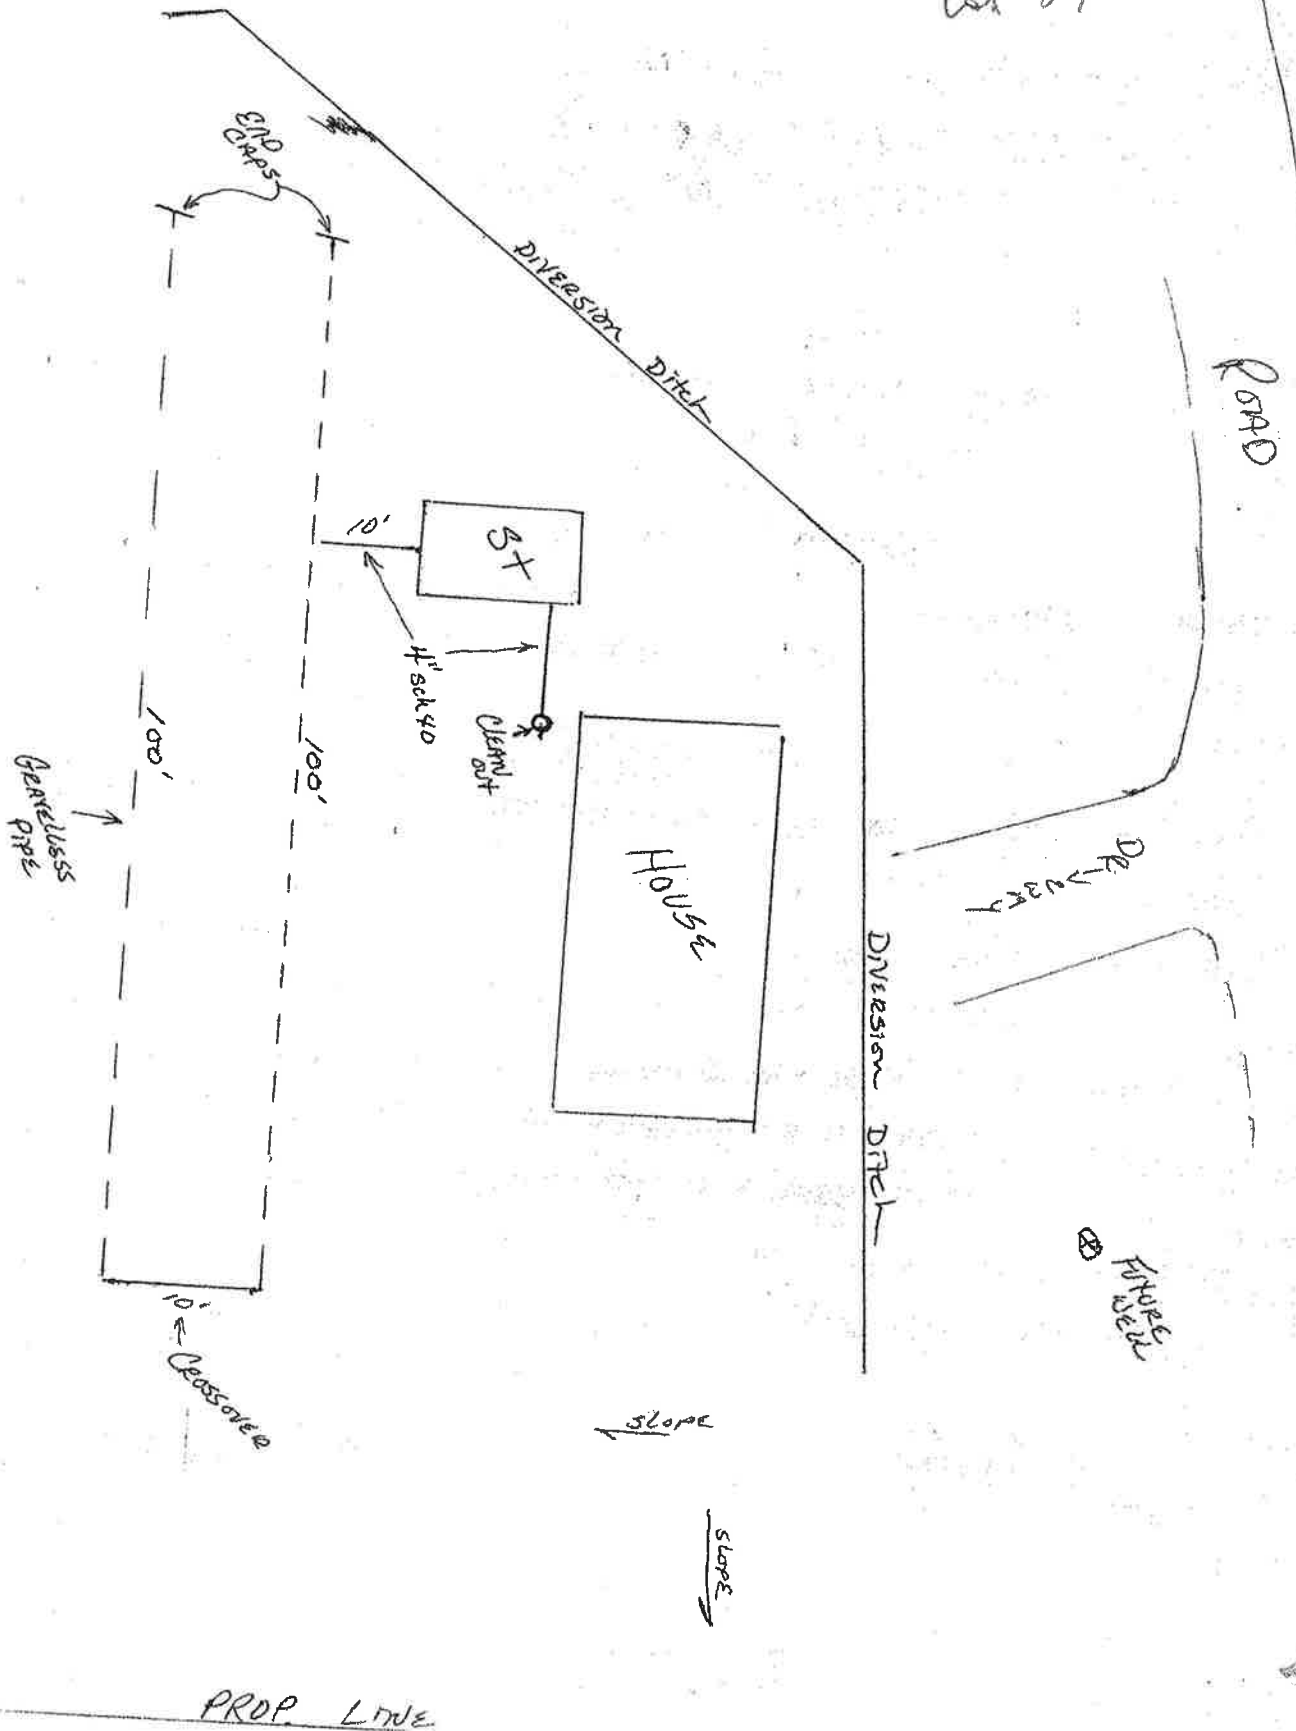

WV STATE DEPARTMENT OF HEALTH
Office of Environmental Health Services
ENVIRONMENTAL ENGINEERING DIVISION

SW25.

WELL COMPLETION REPORT

Date(s) 6/9/93 County Hampshire Permit #: DW-14-04-93-233
 Town: _____ Area Name/Location Whitson Point Lot 25
 Well Owner: Allen C. Ackley Address: 12357 Wadsworth Way
 Telephone Number: 703-590-1378 Woodbridge Va. 22192
 Well Driller: B. Mark Smith Address: HC 86 Box 2-A
 Telephone Number: 304-822-4786 Springfield WV. 26763

WELL LOG

DEPTH IN FEET	FORMATIONS: KIND, THICKNESS, AND IF WATER BEARING	REMARKS:
0-75	Soil / clay + boulders	well was cased to bottom w/ 4" liner bottom 20' perforated
76-105	Sand + gravel	Type of Well: <u>home</u> Drilling Method: <u>Air-hammer</u>
106-164	Driskany	Well Diameter: <u>6 1/4"</u> Casing O.D.: <u>6 5/8"</u>
165-176	fractured formation	Well Depth: <u>206</u> Date Completed: <u>6/9/93</u>
177-184	Driskany	CASING: Length <u>125</u> Feet Height above ground <u>1</u> Feet
185-	water	<input checked="" type="checkbox"/> Steel <input type="checkbox"/> Plastic <input type="checkbox"/> Cast Iron
186-206	Driskany	Other _____ Type _____
		SCREEN
		<input checked="" type="checkbox"/> None Installed
		Type _____ Diameter _____
		Slot/Gauge _____ Length _____
		Set Between _____ Ft. and _____ Ft.
	1800 Gph.	

PUMPING OR BAILING TEST

DETAILS	#1	#2	#3
Static Water Level (Ft. Below Grade)	<u>125</u>		
Pumping Rate (GPM)	<u>30</u>		
Pumping Level (Ft Below Grade)	<u>185</u>		
Duration of Test (In Hours)	<u>1</u>		
Recovery Time to Static Level (In Hours)	<u>1/10</u>		

WELL HEAD

Pitless Adapter: Type, Make, Etc. _____
 Well Cap: Type, Make, Etc. Standard
 Well Seal: Type, Make, Etc. _____
 Well Platform: _____
 Length _____ Width _____ Thickness _____
 Grouting: ☒ Yes ☐ No Pressure
 All Public Water Supplies must be grouted.

I hereby certify that this well was drilled and constructed under my supervision, in compliance with all requirements of the referenced permit, and that this record is true to the best of my knowledge and belief.

B. Mark Smith DD1
 Name Certification No.
B.W. Smith Well Drilling
 Registered Business Name
Benjamin Mark Smith
 Signed Date 6/9/93



Hampshire County Health Department

HC 71, Box 9

Augusta, WV 26704

Nursing: (304) 496-9640 Environmental: (304) 496-9641

Fax: (304) 496-9650

02/22/2012

Allen & Ellen Ackley
2548 Clarence Taylor Rd
Springfield, WV 26763

Dear Allen & Ellen Ackley;

At your request a site visit was made to your property, Lot #25 Whitson Pt Subdivision. A small sewage disposal installation permit was issued 8/20/1994; however the system was installed without a final inspection. A visit to the site on 02/17/2012 indicated 1000 gallon concrete tank had been installed and the baffles were in good condition. The tank was pumped by Carroll's Septic Service on 02/17/2012. The drain field size and type could not be determined since there was no final inspection performed; however there were no visible failures.

Sincerely,


Derrick Haggerty
Sanitarian/Hampshire County Health Dept
