

Hampshire County Health Department On-Site Sewage Disposal System Inspection Form

Permit # **ST-14-08-150**

Name of Owner: William Smith Installer: Ricky S Ramey
 Address: HC 71 Box 59, Augusta, WV 26704
 Property Location: Timber Mtn Rd. Lot Size: 1.687 AC Acres
 Type of Facility: Residence Facility is: ☒ New ☐ Existing
 Design Loading in gpd/# Bedrooms: 3 Source of Water: Well

SEWAGE TANK COMPONENT

Capacity in Gallons: 1000 Material: precast concrete Manufacturer: Jb/12
 Pump Chamber gal
 Distances (in feet) of Tank to: Dwelling 16
 Private ☒ Public ☐ Water Source: 110 Property Line: 10+

ON-SITE DISPOSAL SYSTEM

Class I Systems: Standard Soil Trenches () or Bed () Gravelless Pipe (), Diameter In.
 Chamber Soil Absorption Trenches (X) or Bed ()
 Class II Systems: Pumped/Dosed Soil Absorption Trenches () or Bed ()
 Evapotranspiration Trenches () or Bed ()
 Shallow Soil Absorption Trenches () or Bed () Other:

No. of Lines: 3 Length (in feet) of Each: 80, 80, 80
 Width of Trenches: 36 inches/feet Depth to Bottom of Field: 24 inches
 If Bed, Dimensions (in feet): If Chamber System, Name: 12V-4, No. of Units: 60
 Approved and Adequate Materials Used? Yes (X) No () Size Equates to 1200 sq ft of SGF
 Distance (in feet) of System to: Dwelling 25 Private (X) Public ()
 Water Source: 120 Property Line: 10+

Remarks:

GPS: N39 16 51.1 W78 30 37.9

An inspection indicates that
 The sewage disposal system
 Described above

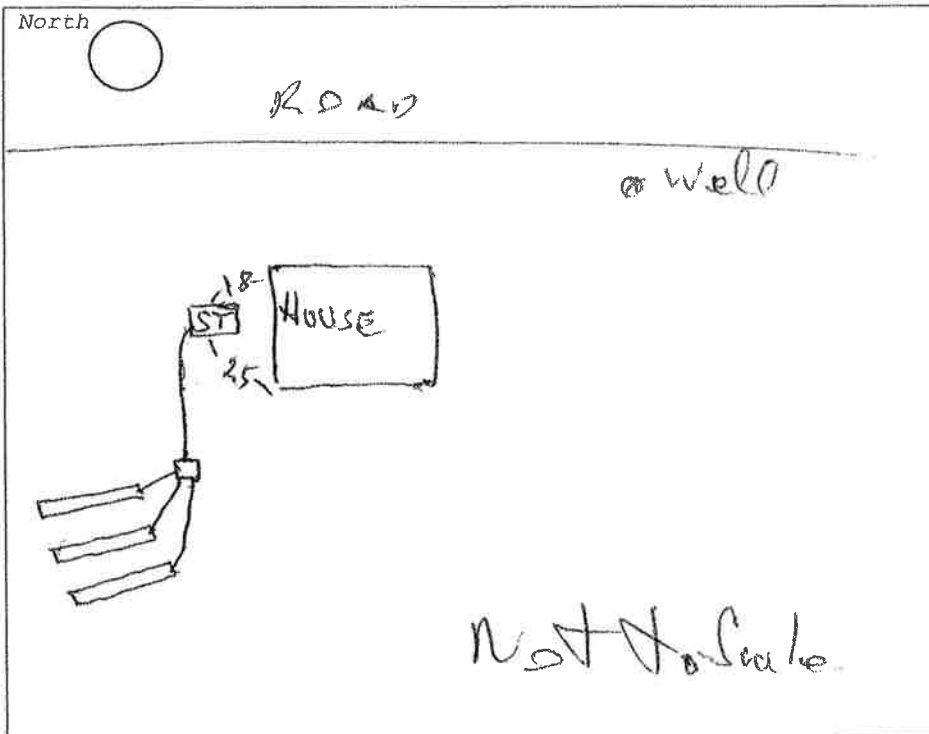
DOES MEET ☒DOES NOT MEET ☐ or

CANNOT BE DETERMINED TO

MEET ☐ the minimum standards
 Established by the West Virginia
 Bureau of Public Health.

To correct a health hazard,
 Modifications to existing systems
 May be done to improve part of a
 System. Such modifications may
 Not be able to be designated as
 a Does meet system since
 Inadequate information is known.

Although many factors
 Contribute to the successful
 Functioning of a sewage disposal
 System, this office recommends
 Water conservation and
 Maintaining an even usage of
 Water throughout the week.

Visit Date(s): 7-6-2008FINAL INSPECTION DATE: 7/18/2008SANITARIAN: J. K. Ramey
