

Hampshire County Health Department On-Site Sewage Disposal System Inspection Form

Permit # **ST-14-15-24**

Name of Owner: David & Elizabeth Sworobuk Installer: Gary Mullins
Address: 3821 Benton St. N.W., Washington, DC 20007
Property Location: Whitson's Point Lot 33 Lot Size: 3 acres
Type of Facility: new Facility is: ☒ New ☐ Existing
Design Loading in gpd/# Bedrooms: 2 Source of Water: well

SEWAGE TANK COMPONENT

Capacity in Gallons: 1000 Material: precast concrete
Distances (in feet) of Tank to: Dwelling NA
Private ☒ Public ☐ Water Source: >100' Property Line: >100'

ON-SITE DISPOSAL SYSTEM

Class I Systems: Standard Soil Trenches () or Bed () Gravelless Pipe (), Diameter In.
Chamber Soil Absorption Trenches (☒) or Bed ()
Class II Systems: Pumped/Dosed Soil Absorption Trenches () or Bed () LPP ()
Evapotranspiration Trenches () or Bed ()
Shallow Soil Absorption Trenches () or Bed () Other:

No. of Lines: 3 Length (in feet): 80's
Width of Trenches: 36 inches/feet Depth to Bottom of Field: 24 inches
Size Equates to 1200 sq ft of SGF
Distance (in feet) of System to: Dwelling NA
Private (☒) Public () Water Source: >100' Property Line: >100'
Remarks: dwelling not constructed at time of inspection
GPS: N39 28 37.7 W78 37 39.1

An inspection indicates that
The sewage disposal system
Described above

DOES MEET ☒

DOES NOT MEET ☐ or


CANNOT BE DETERMINED TO

MEET ☐ the minimum standards
Established by the West Virginia
Bureau of Public Health.

To correct a health hazard,
Modifications to existing systems
May be done to improve part of a
System. Such modifications may
Not be able to be designated as
a Does meet system since
Inadequate information is known.

Although many factors
Contribute to the successful
Functioning of a sewage disposal
System, this office recommends
Water conservation and
Maintaining an even usage of
Water throughout the week.

Visit Date(s): 9/23/2014

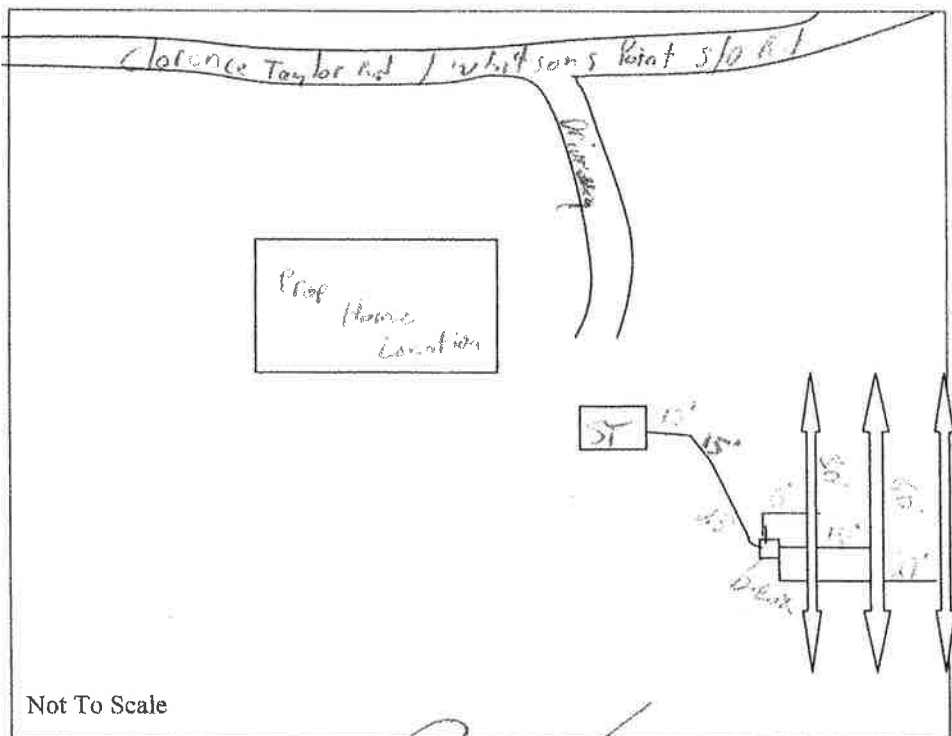

FINAL INSPECTION DATE: 9/23/2014

SANITARIAN: RNL



Hampshire County Health Department

HC 71, Box 9

Augusta, WV 26704

Nursing: (304) 496-9640 Environmental: (304) 496-9641

Fax: (304) 496-9650

11/28/2012

Hampshire County Planning Commission
PO Box 883
Romney, WV 26757

Dear Sirs:

This office has reviewed a plat of survey for Robin Hardy to approve 2 lots at Whitsons Point Subdivision, and further referenced as Tax District Springfield, Tax Map 20, Parcel 105 & 103, Deed book 506, Page 688. This subdivision consists of 2.79 & 2.98 acres. All lots require a percolation test and a sewage disposal area of 10,000 square feet where no development or structures other than the septic system shall be permitted. These lots are to be developed with individual wells and septic systems to serve single family dwellings.

Percolation test results are within limits as set forth by West Virginia CRS 16-1. Six foot soil observation holes indicate no restrictions due to water table or shallow bedrock within the designated sewage disposal area except as noted on the Health Department subdivision application.

The plat of survey dated 11/26/2012, is hereby approved by the Hampshire County Health Department. Any changes or revisions to the Health Department stamped and signed plat, or subsequent final plats approved based upon the approved plat, will make this approval null and void.

This approval is not permit for individual water systems or individual sewer systems. Applications for permits must be made separately to the Hampshire County Health Department.

Sincerely,

A handwritten signature in dark ink, appearing to read "Derrick A. Haggerty", with a long, sweeping horizontal line extending to the right.

Derrick A. Haggerty

CC: Robin Hardy

2nd page letter of approval for

Subdivision Name: Whitson's Point
Total # of Lots: _____ Name of Applicant: Mu'd J. Sward BUK
Name of Certified Installer Responsible for Testing: WALTER FIELD'S
Installer Certification #: 154-05-A-0057
Installer Signature: Walter Field's Date: 11-16-12
Installer Address: HC 8, Box 354 Grosbeak Springs, WV

[illegible]

B.W. Smith Well Drilling, Inc.
P.O. Box 440
Springfield, WV 26763
(304)496-9977

ATTN: Keenan

Date: 11-12-12

On Nov. 8, a well yield test was performed and the frost-free hydrant was replaced at Lots 31&33 at Whitson's Point in Springfield, WV. The well was determined to be in working condition and can be used as a source of potable water.

Jon T. Moyer
